1 Close EB S.R. 434 entrance ramp to WB I-4

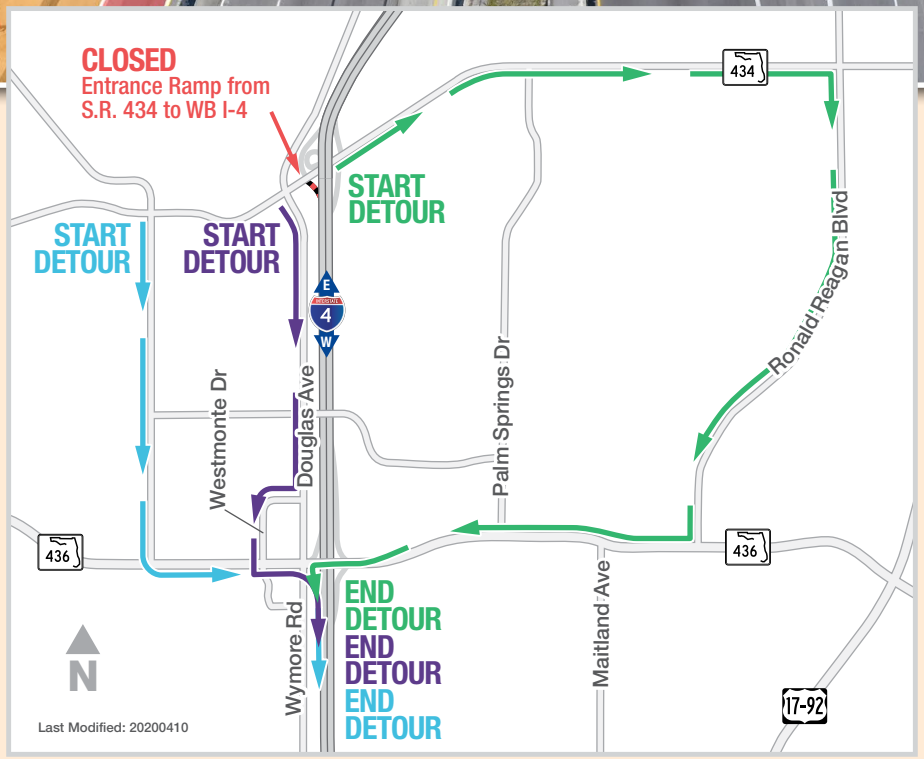

© Florida Department of Transportation

2 S.R. 50 road closures to expedite bridge construction

Multiple weekend closures of S.R. 50 under I-4 in downtown Orlando to expedite the construction of the I-4WB overpass.

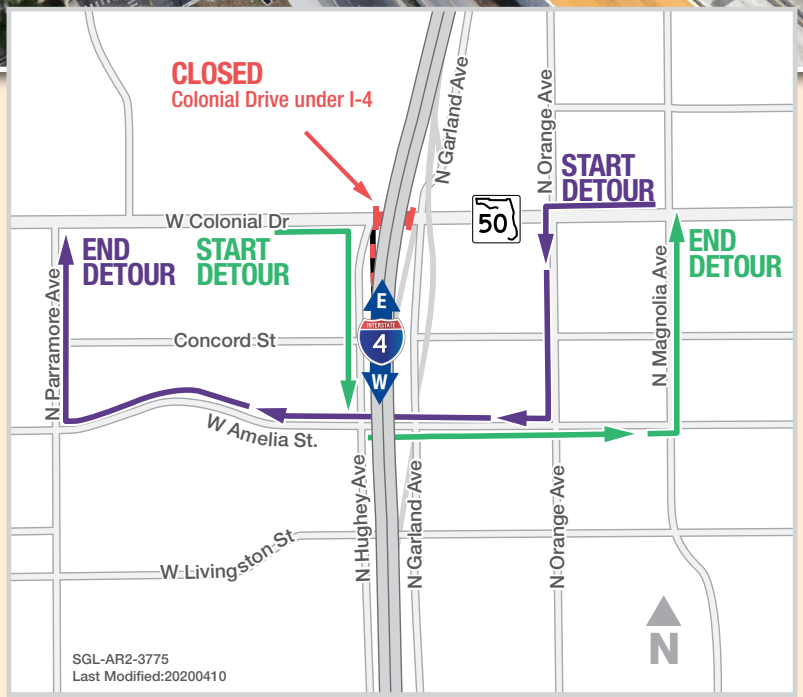

© Florida Department of Transportation

3 I-4 WB crossover Livingston to Amelia

Two week continuous single lane closure, in a three-lane section of I-4, to implement pavement tie ins. Followed by one (1) weekend full closure and detour of westbound I-4 from Lee Road through John Young Parkway to implement shift onto crossover.

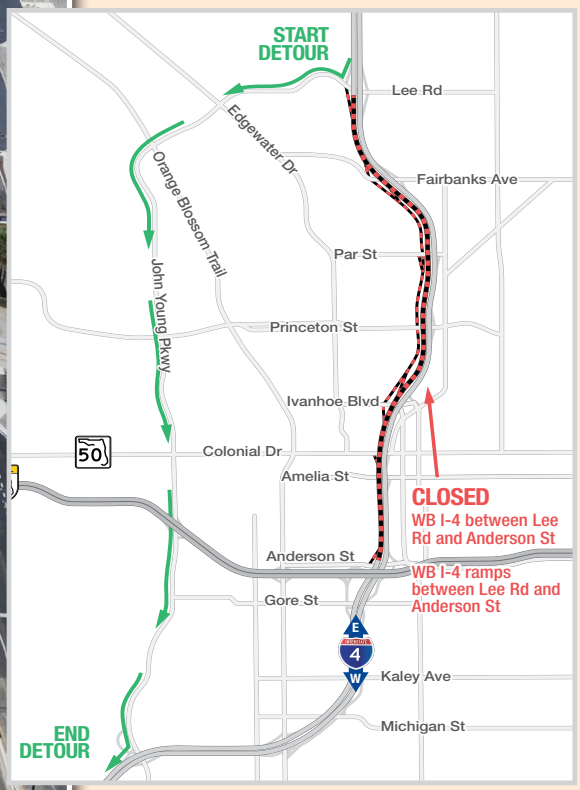

© Florida Department of Transportation

4 I-4 / S.R. 408 Interchange Flyover Bridges

Implementing operations 1, 2, 3 and 5 promote opening the new I-4 to S.R. 408 flyover ramps as much as 1–2 months sooner than currently projected. This greatly reduces congestion through the most heavily traveled interchange within the I-4 Ultimate project. In conjunction, approximately 2 miles of new WB I-4 GUL though downtown Orlando become available to motorists.

Ramps to be opened shown below and at right

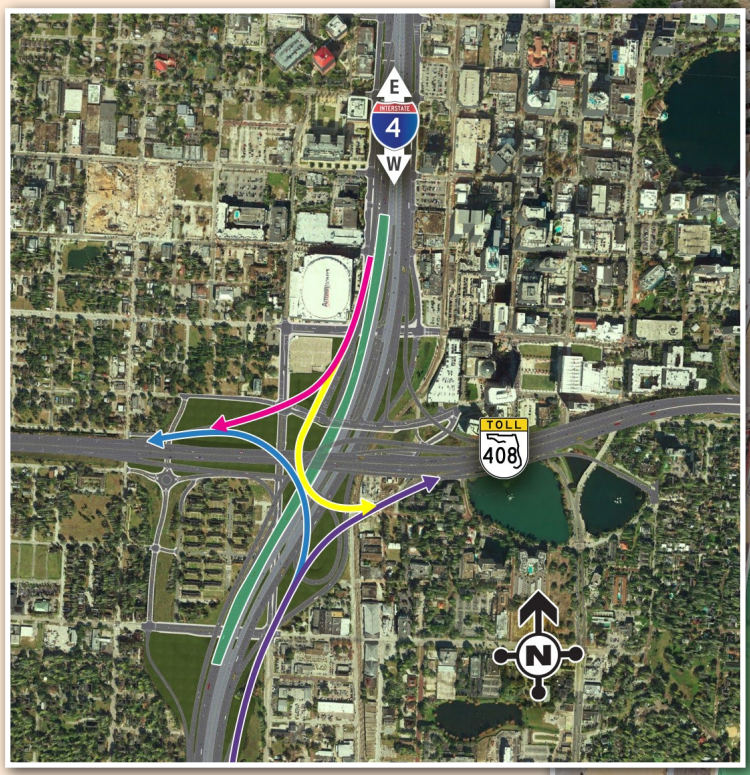

© Florida Department of Transportation

5 Extended Daytime Mainline Lane Closures

Expand lane closure hours. Locations will vary each week, with select areas using 24-Hour closures for up to two (2) weeks.

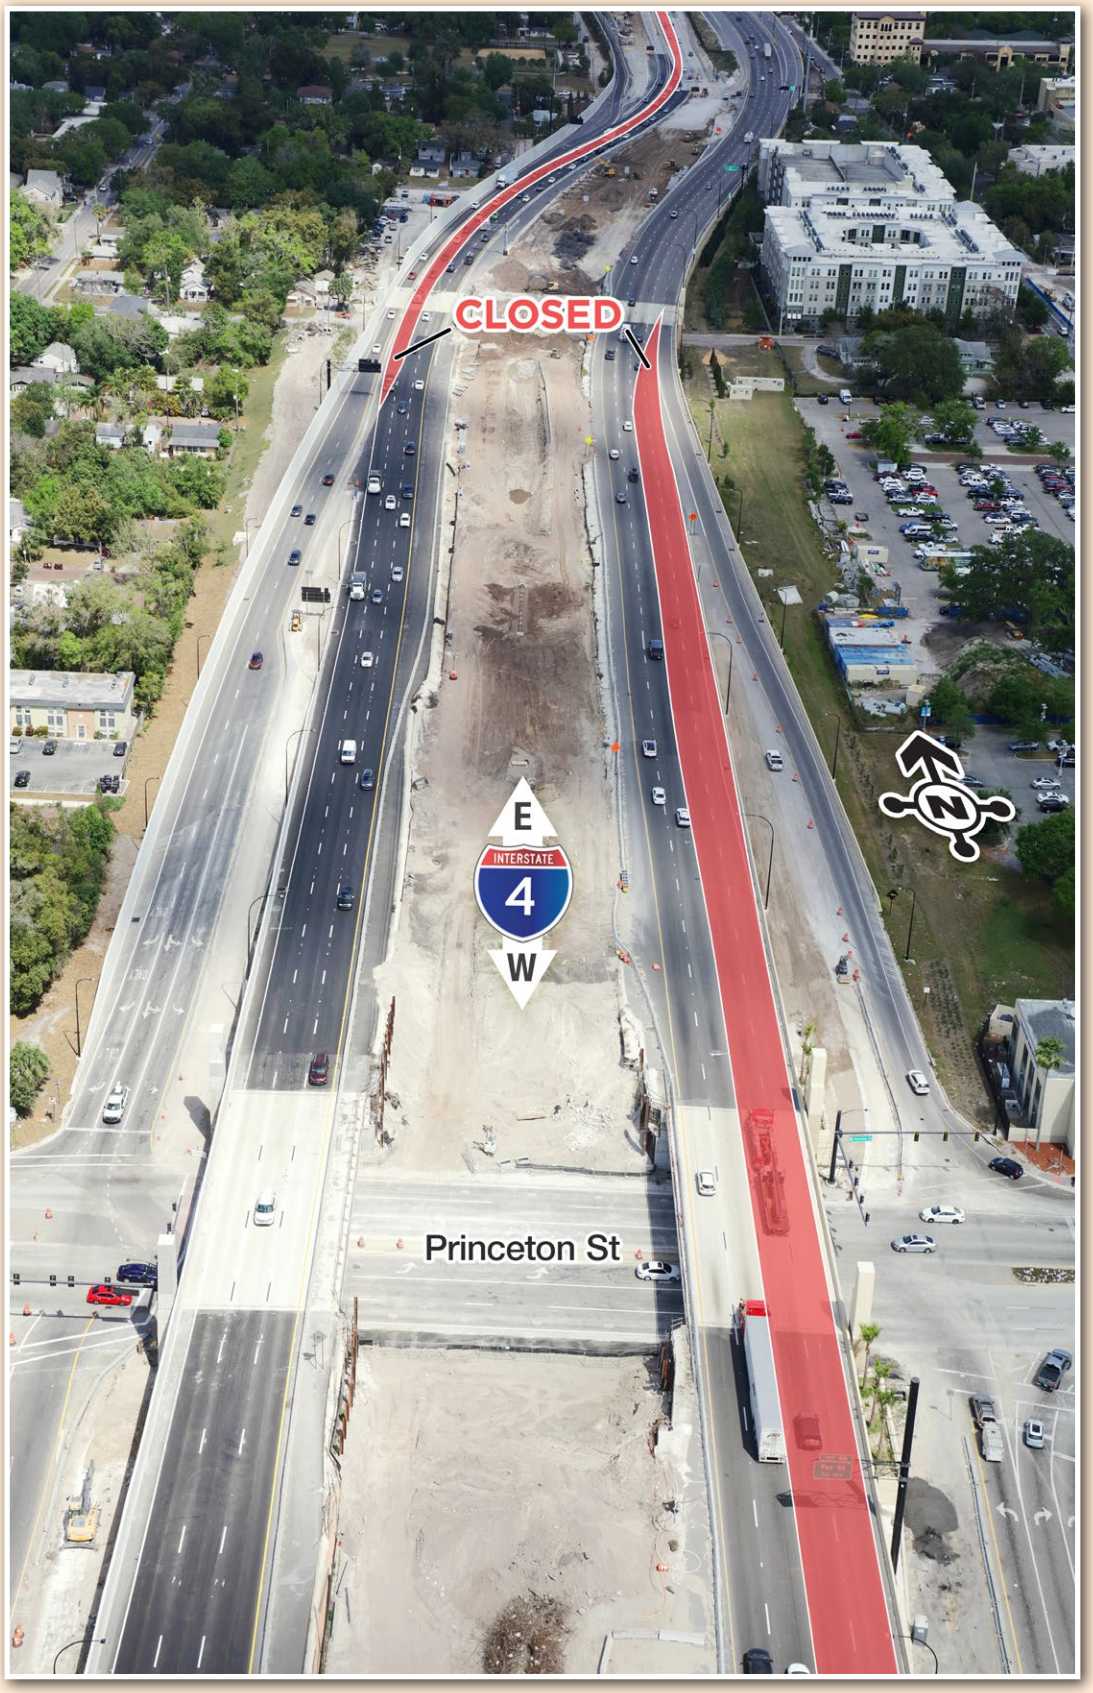

© Florida Department of Transportation
